


## **Diary**


### **New Platform**

June 7, 2024 New Platform Drawing FSK019-2 Rev3 JMG 07/06/24

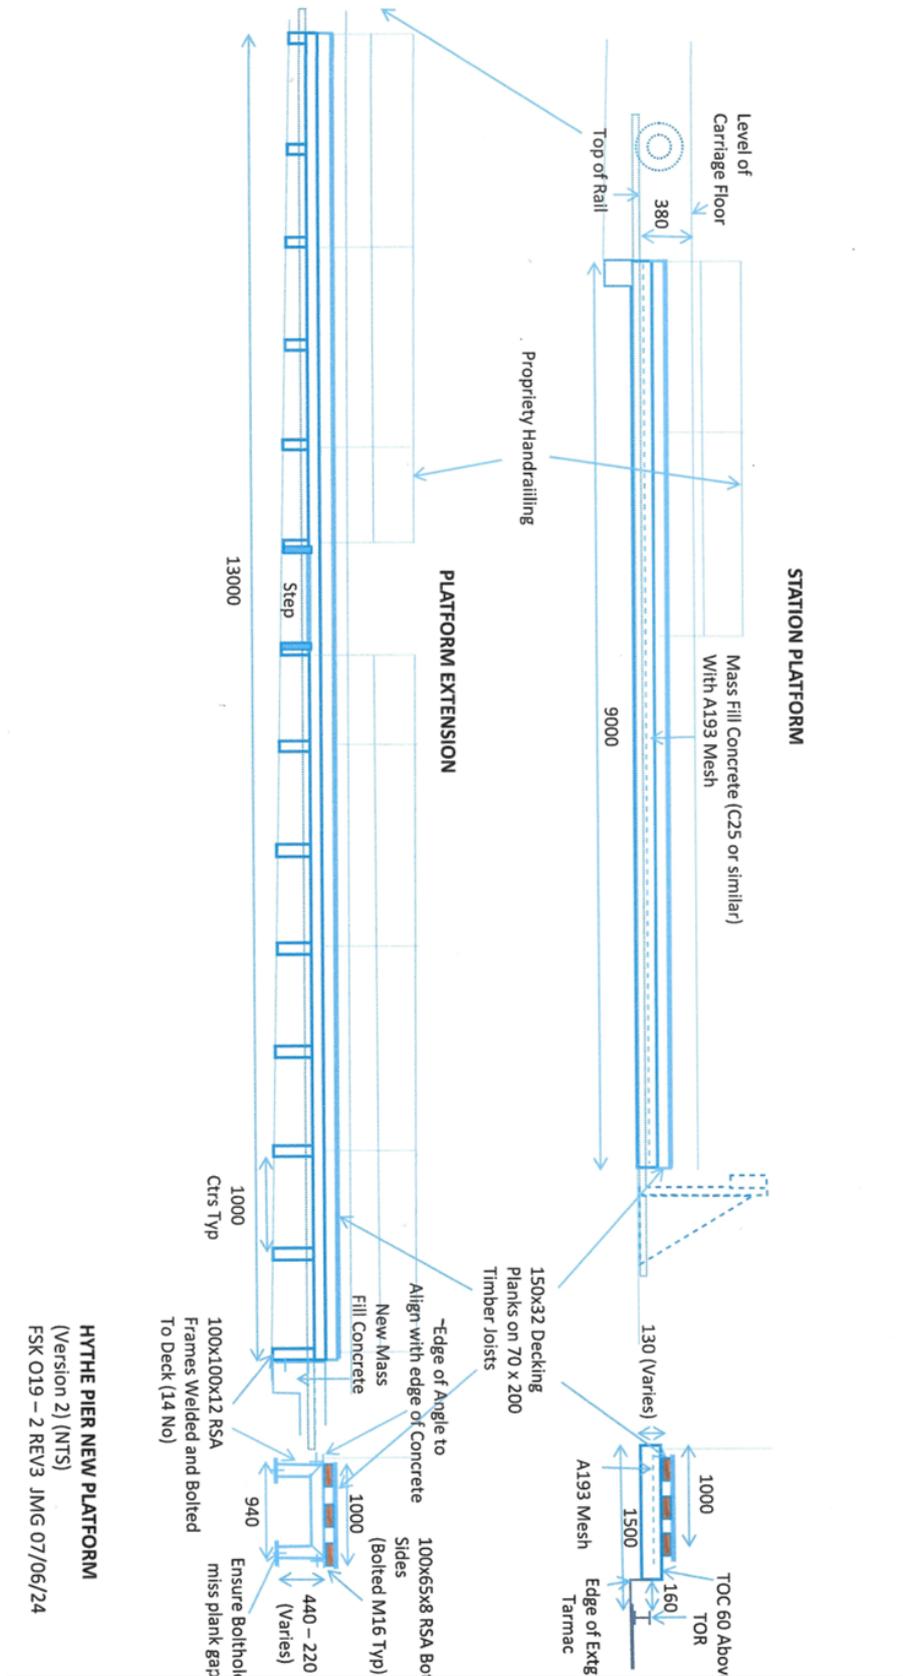


HYTHE PIER NEW PLATFORM  
 (Version 2) (NTS)  
 FSK 019 - 2 REV3 JMG 07/06/24

**June 11, 2024 – Shuttering for concrete pour**

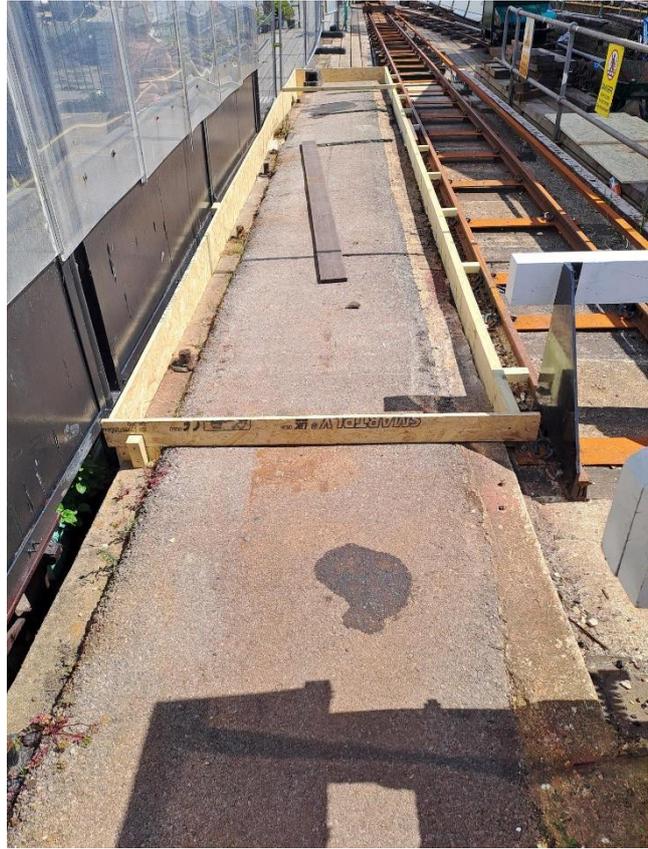


*Photos: Alan Titheridge*

## June 13, 2024 – Pouring of Concrete

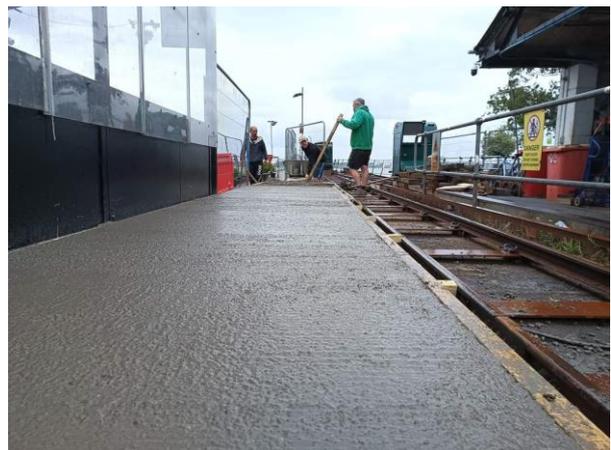

Photographs – John Greenwood

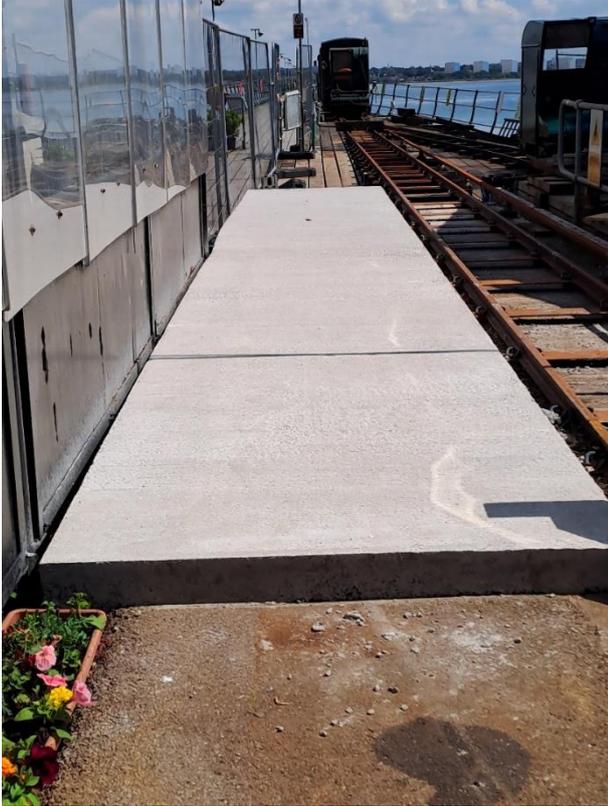


**June 20, 2024 – Shuttering removed**


*Photographs: Alan Titheridge*



## July 8, 2024 – Installation of Platform Support Ironwork

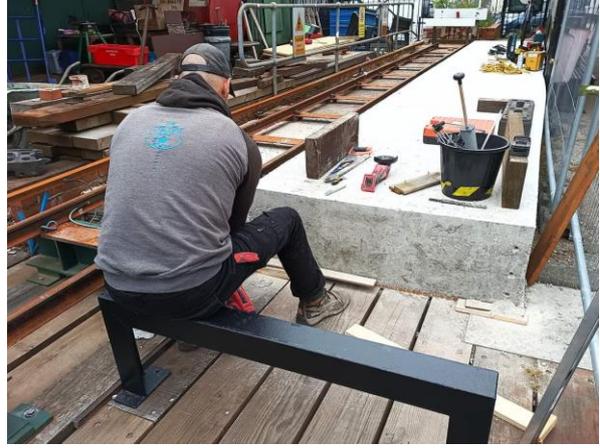

*Photos Above and Below: John Greenwood*

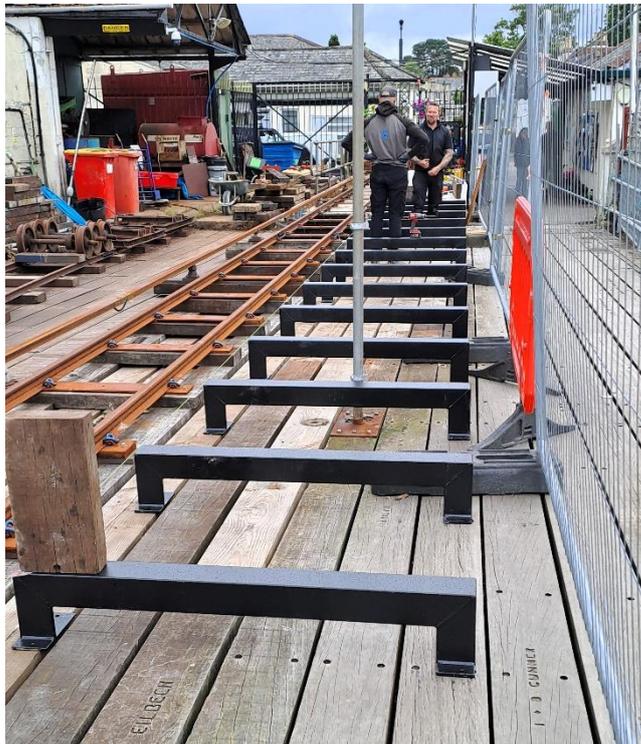

*Photo: Alan Titheridge*



**July 9, 2024 – Completion of Platform Support Ironwork**



*Photos: Above left - Alan Titheridge, other 3 John Greenwood*



**July 10, 2024 – Laying out of timber**

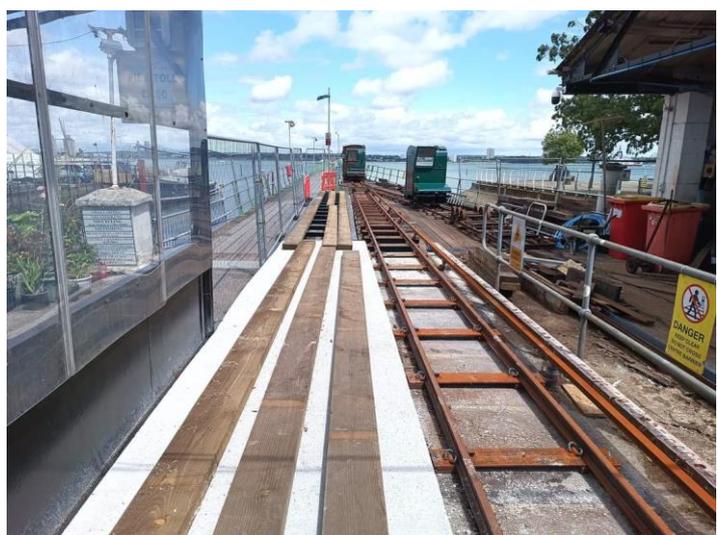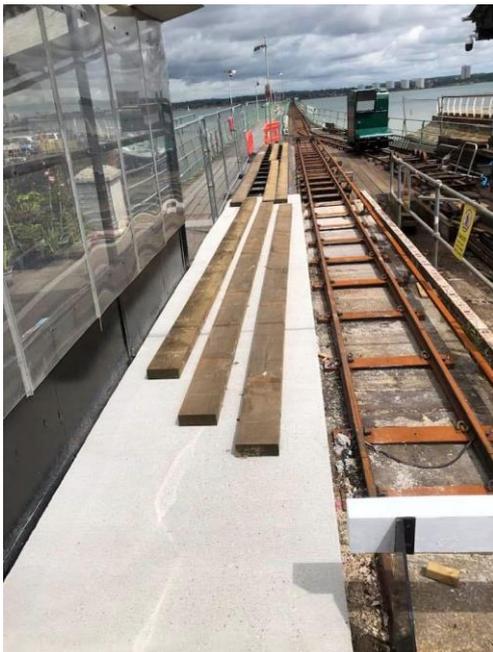

*Photos: Allan Fairhead*



**July 11, 2024 – Securing first deck beam**

*Above and Below Left: Photo John Greenwood, Below Right: Photo Alan Titheridge*



**July 16, 2024 – Removal of lamppost**



*Photos: John Greenwood*





**July 18, 2024 – Completion of the securing of deck beams.**

*Photos: John Greenwood*



**July 31, 2024 – Application of decking oil to beams**

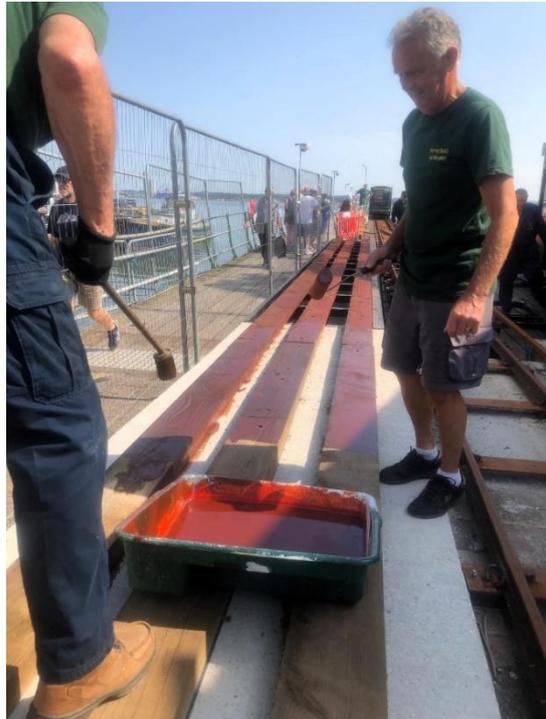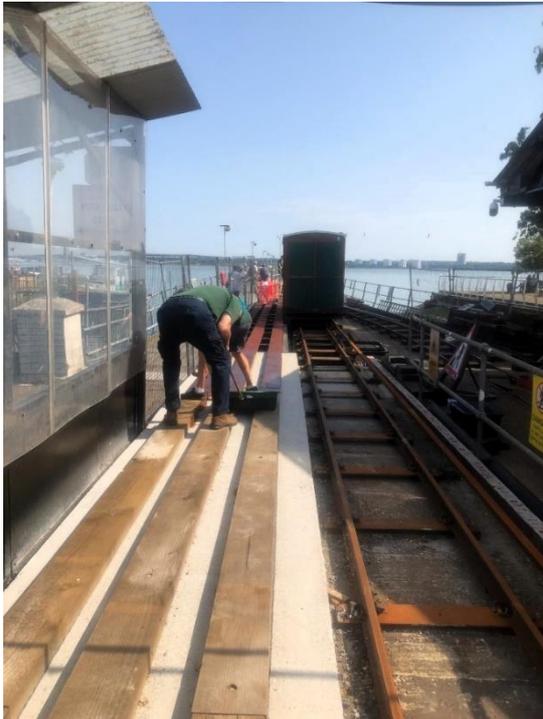

*Photos: Tina Brown*

**August 7, 2024 –  
Final preparation in  
advance of laying of  
decking**

*Photos: John Greenwood*




**August 14, 2024 - Laying of decking - August 17, 2024**



*Photos: Above John Greenwood and Right: Alan Titheridge*




**August 20, 2024 – Decking almost laid**

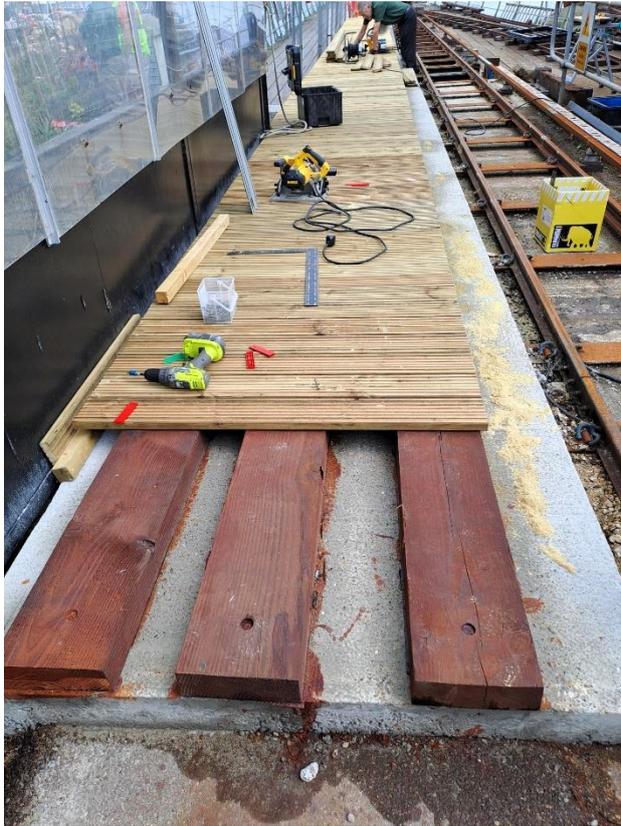

*Photos: Alan Titheridge*



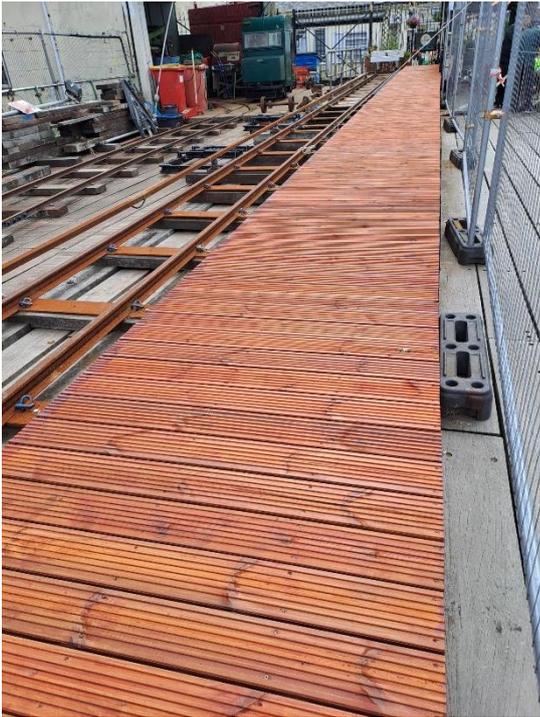

## August 29, 2024 – Decking fully coated

Platform decking fully stained with Barrentine decking oil, red cedar.

(Photo: Alan Titheridge)

## September 17, 2024 – Arrival of handrail tubes

Arrival of tubes and furniture for slope handrails.

Photo: John Greenwood



## September 19, 2024 – Arrival of Platform Fencing



Photos: Upper Allan Fairhead, Lower HPHA.

